Airport Link Schedule
As of June 2008
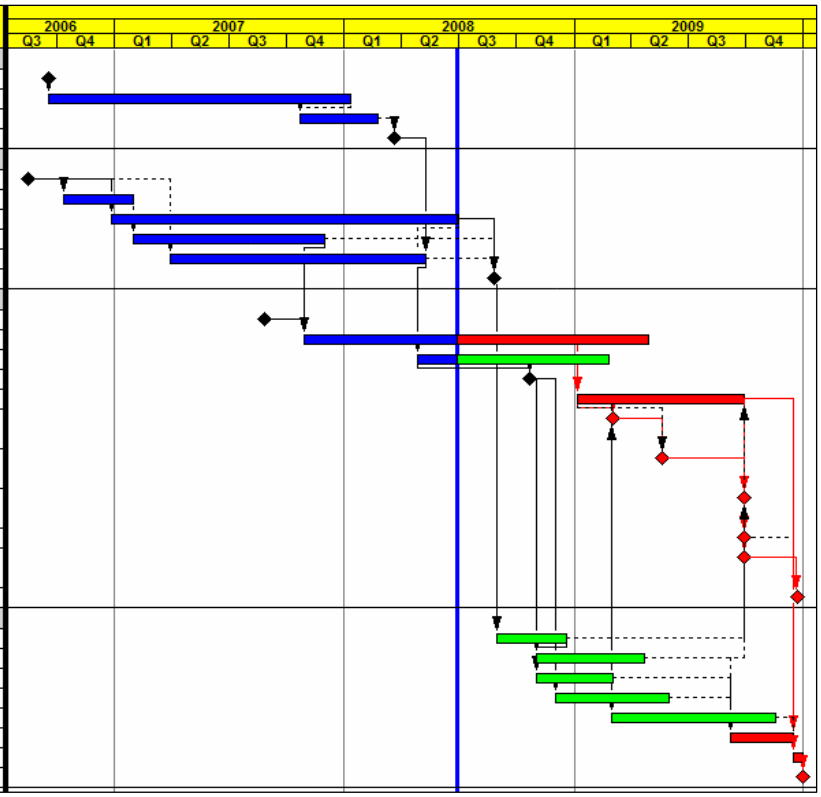
Activity Description	Early Start	Early Finish
410 - S. 154th St. to 160th St.		
NTP	18SEP06A	
Aerial Guideway/At-Grade	18SEP06A	11JAN08A
Trackwork 154th to 160th	22OCT07A	22FEB08A
Substantial Completion		20MAR08A
420 - S. 160th St. to Airport Station		
NTP	17AUG06A	
Demo Station Site, Relocations &	13OCT06A	29JAN07A
Elevated Guideway	27DEC06A	30JUN08
Station Foundations	30JAN07A	30NOV07A
At-Grade Guideway	30MAR07A	09MAY08A
Substantial Completion		26AUG08
430R - Airport Station & Trackwork		
NTP -Station Construction	28AUG07A	
Station Structure Construction	29OCT07A	29APR09
Trackwork Construction	28APR08A	24FEB09
MS 1 Rail Complete to Xover		22OCT08
Station Roof, Finishes, Ped Bridge	06JAN09	28SEP09
MS 2 Station Electrical & Comm Rooms Complete		02MAR09
MS 4 Initial Sta. Electrical Rough -In Complete		21MAY09
MS 8 Substantial Completion Except Ground Plane		28SEP09
MS 9 Temporary Occupancy Permit		28SEP09
MS 10 Substantial Completion Ground Plane		28SEP09
MS 11 Final Acceptance		21DEC09
Follow On Contracts		
C431 TPSS Site	01SEP08	19DEC08
C843 Communications	03NOV08	21APR09
C842 Signals	03NOV08	02MAR09
C847 OCS	02DEC08	30MAY09
Port Pedestrian Bridge	02MAR09	16NOV09
System Integration, Testing &	07SEP09	15DEC09
Systemwide Float to Compl.	16DEC09	31DEC09
Revenue Service		31DEC09
